

DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

PHASE 1A CONSTRUCTION

- 1. SET UP TRAFFIC CONTROL ADVANCE WARNING SIGNS ON US 60/WICKENBURG WAY AT SOUTH END OF PROJECT.
- 2. SET UP TRAFFIC CONTROL ADVANCE WARNING SIGNS ON US 93/TEGNER ST AT NORTH END OF PROJECT.
- 3. BEGIN CONSTRUCTION OF NEW BRIDGES OVER HASSAYAMPA RIVER AND SOLS WASH. THE SOLS WASH BRIDGE MUST BE COMPLETED WITHIN THE FIRST 9 MONTHS OF THE CONTRACT.
- 4. RELOCATE EXISTING UTILITIES WEST OF SOUTH ROUNDABOUT (SEE UT SERIES SHEETS).
- 5. CONSTRUCT NEW SOUTH ROUNDABOUT.
- 6. BEGIN CONSTRUCTION ON CONTAINMENT BASIN (DETAIL L) AND US 93 ROADWAY EMBANKMENT 500' BOTH LEADING UP TO AND FOLLOWING SOLS WASH BRIDGE.
- 7. CONSTRUCT ALL DRAINAGE AND STORM DRAIN CULVERTS WITHIN THE LIMITS INDICATED IN ITEM 6.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	147	380	
93 MA 198					



To Kingman

TEGNER STREET (US 93)

Exst Bridge  
To Remain

SEWER  
RELOCATION

WICKENBURG  
WAY (US 60)

WATER  
RELOCATION

CABLE & POWER  
RELOCATION

SOLS WASH IMPROVEMENTS  
BY OTHERS

CONTAINMENT BASIN  
SEE DETAIL L

SOLS WASH BRIDGE

HASSAYAMPA

SOUTH ROUNDABOUT

Exst Bridges  
To Remain

HASSAYAMPA RIVER BRIDGE

US 60



To Phoenix

GENERAL NOTES

- 1. MAINTAIN NB & SB TRAFFIC ON EXISTING US 93 AND EB & WB TRAFFIC ON EXISTING US 60.
- 2. CONTRACTOR SHALL NOT CONSTRUCT ANY OF THE EMBANKMENT ALONG THE NEW US 93 AS SHOWN IN PHASE 2A UNTIL THE EXISTING WB US 60 BRIDGE OVER THE HASSAYAMPA RIVER IS COMPLETELY REMOVED AND THE EXISTING EB US 60 BRIDGE IS RAISED.
- 3. COORDINATION WILL BE REQUIRED WITH THE SOLS WASH IMPROVEMENT PROJECT THAT WILL BE CONSTRUCTED CONCURRENTLY BY THE FLOOD CONTROL DISTRICT OF MARICOPA COUNTY (FCDMC).

LEGEND

- Existing Roadway
- Work Area
- Temporary Pavement
- Completed Work

		NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION		
DESIGN	BWS/PJB		06-07			
DRAWN	ASJ/SR		06-07			
CHECKED	BSW		06-07			
 <b>JACOBS</b>				TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 1A		
ROUTE		LOCATION				
US 93		WICKENBURG BYPASS				DWG TC03
TRACS NO. H 5825 01C			NH-093-B(008)B		___ OF ___	


DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	148	380	

93 MA 198

PHASE 1B CONSTRUCTION

1. COMPLETE CONSTRUCTION OF NEW BRIDGE OVER HASSAYAMPA RIVER AND THE SOLS WASH BRIDGE.
2. COMPLETE THE CONSTRUCTION OF THE PORTION OF THE CONTAINMENT BASIN ADJACENT TO THE SOLS WASH BRIDGE AND THE US 93 ROADWAY EMBANKMENT 500' LEADING UP TO AND FOLLOWING THE SOLS WASH BRIDGE.
3. CONSTRUCT NORTH HALF OF TIE-IN TO WICKENBURG WAY.
4. CONSTRUCT NORTH HALF OF TIE-IN TO US 60.
5. CONSTRUCT NEW CURB TO CLOSE THROUGH ACCESS ON APACHE STREET AT THE COMMUNITY CENTER ENTRANCE.

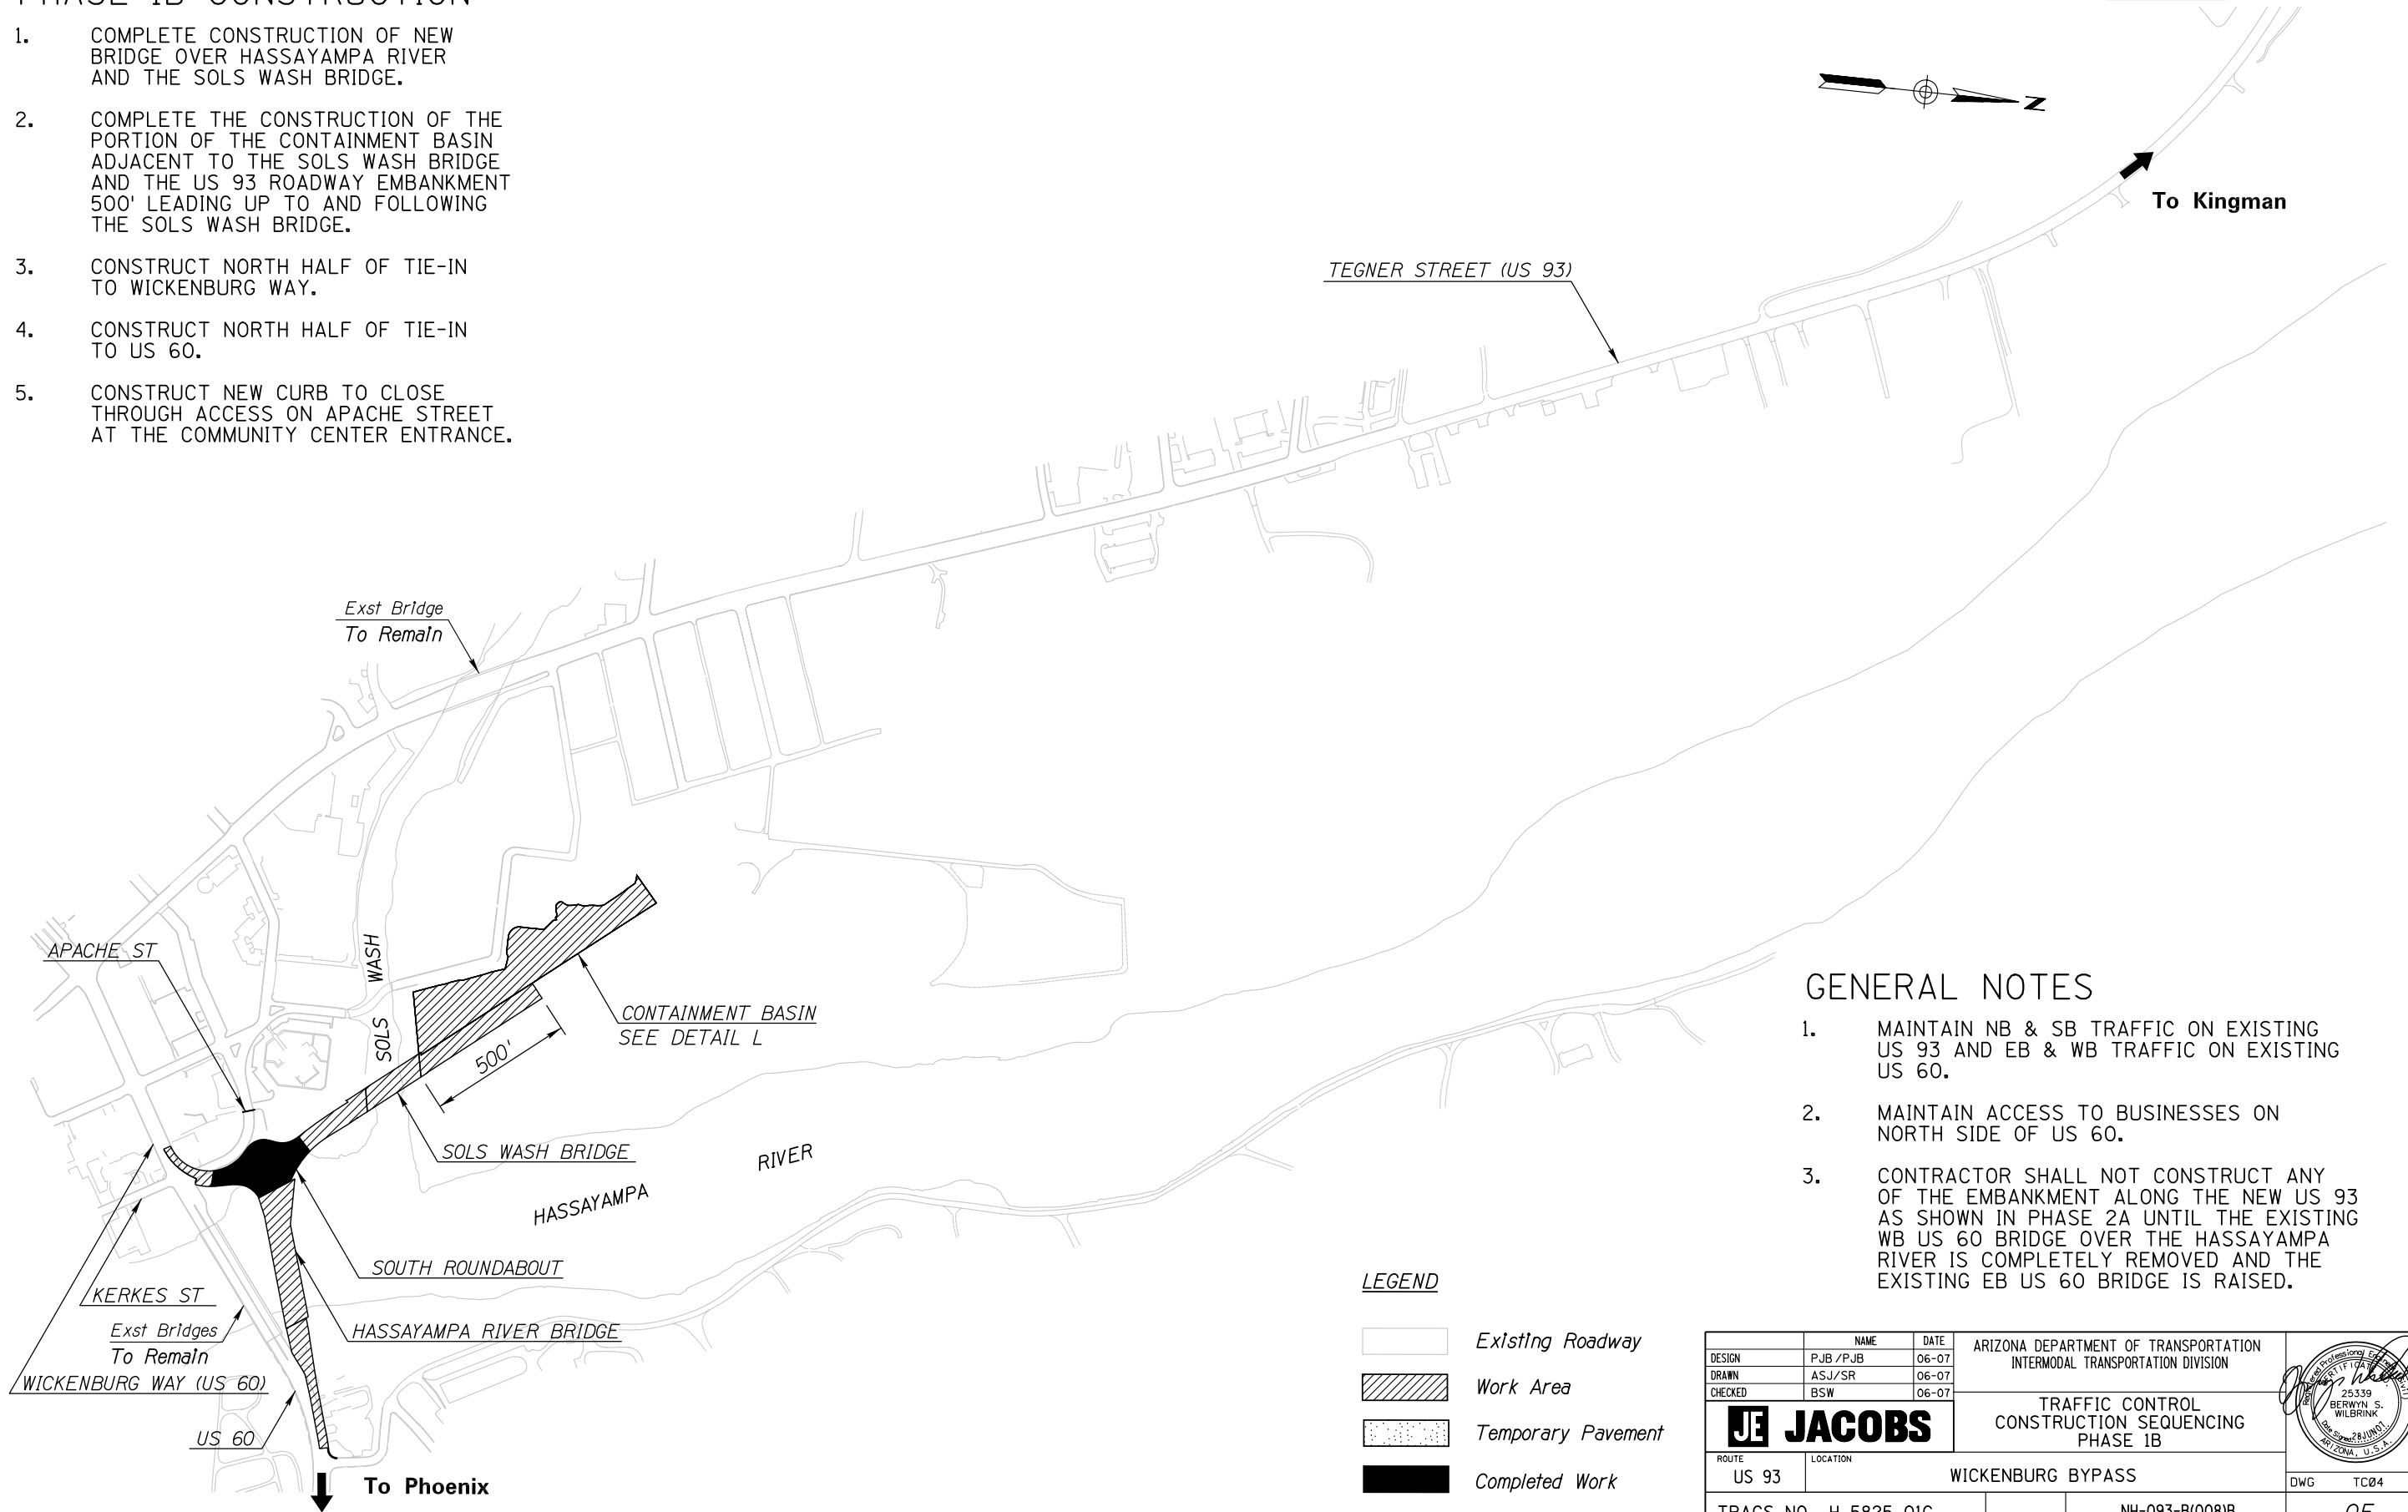


DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	149	380	
93 MA 198					

PHASE 1C CONSTRUCTION

1. CONSTRUCT SOUTH HALF OF TIE-IN TO WICKENBURG WAY AND KERKES STREET.
2. CONSTRUCT SOUTH HALF OF US 60 ROADWAY TIE-IN.
3. FOLLOWING SHIFT OF TRAFFIC TO NEW BRIDGE, TEMPORARILY MOVE SANITARY SEWER FORCE MAIN TO EXISTING WB BRIDGE.
4. RAISE EXISTING EB US 60 HASSAYAMPA RIVER BRIDGE. PAINT EB BRIDGE.
5. SHIFT ALL UTILITIES TO RAISED EB BRIDGE. SEE UT SERIES SHEETS.
6. REMOVE EXISTING WB US 60 HASSAYAMPA RIVER BRIDGE AND PIERS. ABUTMENTS TO REMAIN. SALVAGE PORTION OF WB BRIDGE FOR INTERPRETIVE SITE.
7. CONSTRUCT GATEWAY TREATMENTS AT BOTH ENDS OF OLD BRIDGE LOCATION.



To Kingman

TEGNER STREET (US 93)

Exst Bridge  
To Remain

WICKENBURG WAY  
(US 60)

KERKES ST

WEST GATEWAY

Exst WB Bridge  
Remove

Exst EB Bridge  
To Be Raised

EAST GATEWAY

US 60

SOUTH ROUNDABOUT

HASSAYAMPA

RIVER



To Phoenix

LEGEND

- Existing Roadway
- Work Area
- Temporary Pavement
- Completed Work

GENERAL NOTES

1. SHIFT TRAFFIC TO COMPLETED PORTION OF US 60, THE SOUTH ROUNDABOUT, AND WICKENBURG WAY/US 60.
2. MAINTAIN ACCESS TO BUSINESSES ON US 60.
3. MAINTAIN ACCESS TO KERKES STREET SOUTH OF US 60.
4. CONTRACTOR SHALL NOT CONSTRUCT ANY OF THE EMBANKMENT ALONG THE NEW US 93 AS SHOWN IN PHASE 2A UNTIL THE EXISTING WB US 60 BRIDGE OVER THE HASSAYAMPA RIVER IS COMPLETELY REMOVED AND THE EXISTING EB US 60 BRIDGE IS RAISED.

		NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION			
DESIGN	PJB /PJB		06-07	TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 1C			
DRAWN	ASJ/SR		06-07				
CHECKED	BSW		06-07				
							
ROUTE		LOCATION				DWG	
US 93		WICKENBURG BYPASS				TC05	
TRACS NO. H 5825 01C				NH-093-B(008)B		___ OF ___	

DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	150	380	

93 MA 198

PHASE 2A CONSTRUCTION

1. CONSTRUCT NB AND SB US 93 FROM 500' NORTH OF THE SOLS WASH BRIDGE TO THE NORTH ROUNDABOUT.
2. CONSTRUCT US 93 FROM NORTH ROUNDABOUT TO EXISTING US 93. CONSTRUCT EAST HALF OF TIE-IN TO EXISTING US 93.
3. CONSTRUCT ACCESS ROAD.
4. STRIPE COMPLETED US 93 AND ACCESS ROAD.



To Kingman

TEGNER STREET (US 93)

ACCESS ROAD

NORTH ROUNDABOUT

Exst Bridge  
To Remain

US 93

RANCHO DEL RIO

WASH

SOLS

RIVER

HASSAYAMPA

SOUTH ROUNDABOUT

KERKES ST

WICKENBURG WAY (US 60)

US 60

To Phoenix

GENERAL NOTES

1. MAINTAIN TRAFFIC ON COMPLETED PORTION OF US 60/WICKENBURG WAY.
2. MAINTAIN ACCESS TO PROPERTIES ALONG ACCESS ROAD.

LEGEND

- Existing Roadway
- Work Area
- Temporary Pavement
- Completed Work


DESIGN	NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION
DRAWN	BSW/PJB	06-07	
CHECKED	ASJ/SR	06-07	
	BSW	06-07	
<b>JE JACOBS</b>			TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 2A
ROUTE	LOCATION		DWG
US 93	WICKENBURG BYPASS		TC06
TRACS NO. H 5825 01C		NH-093-B(008)B	OF

DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	151	380	
93 MA 198					

PHASE 2B CONSTRUCTION

1. CONSTRUCT WEST HALF OF NEW US 93 TIE-IN TO EXISTING US 93.
2. CONSTRUCT NEW TEGNER STREET ROADWAY AND DRIVEWAYS.
3. REMOVE OLD PORTION OF TEGNER STREET FROM NEW TEGNER STREET TIE-IN TO NEW US 93 TIE-IN.

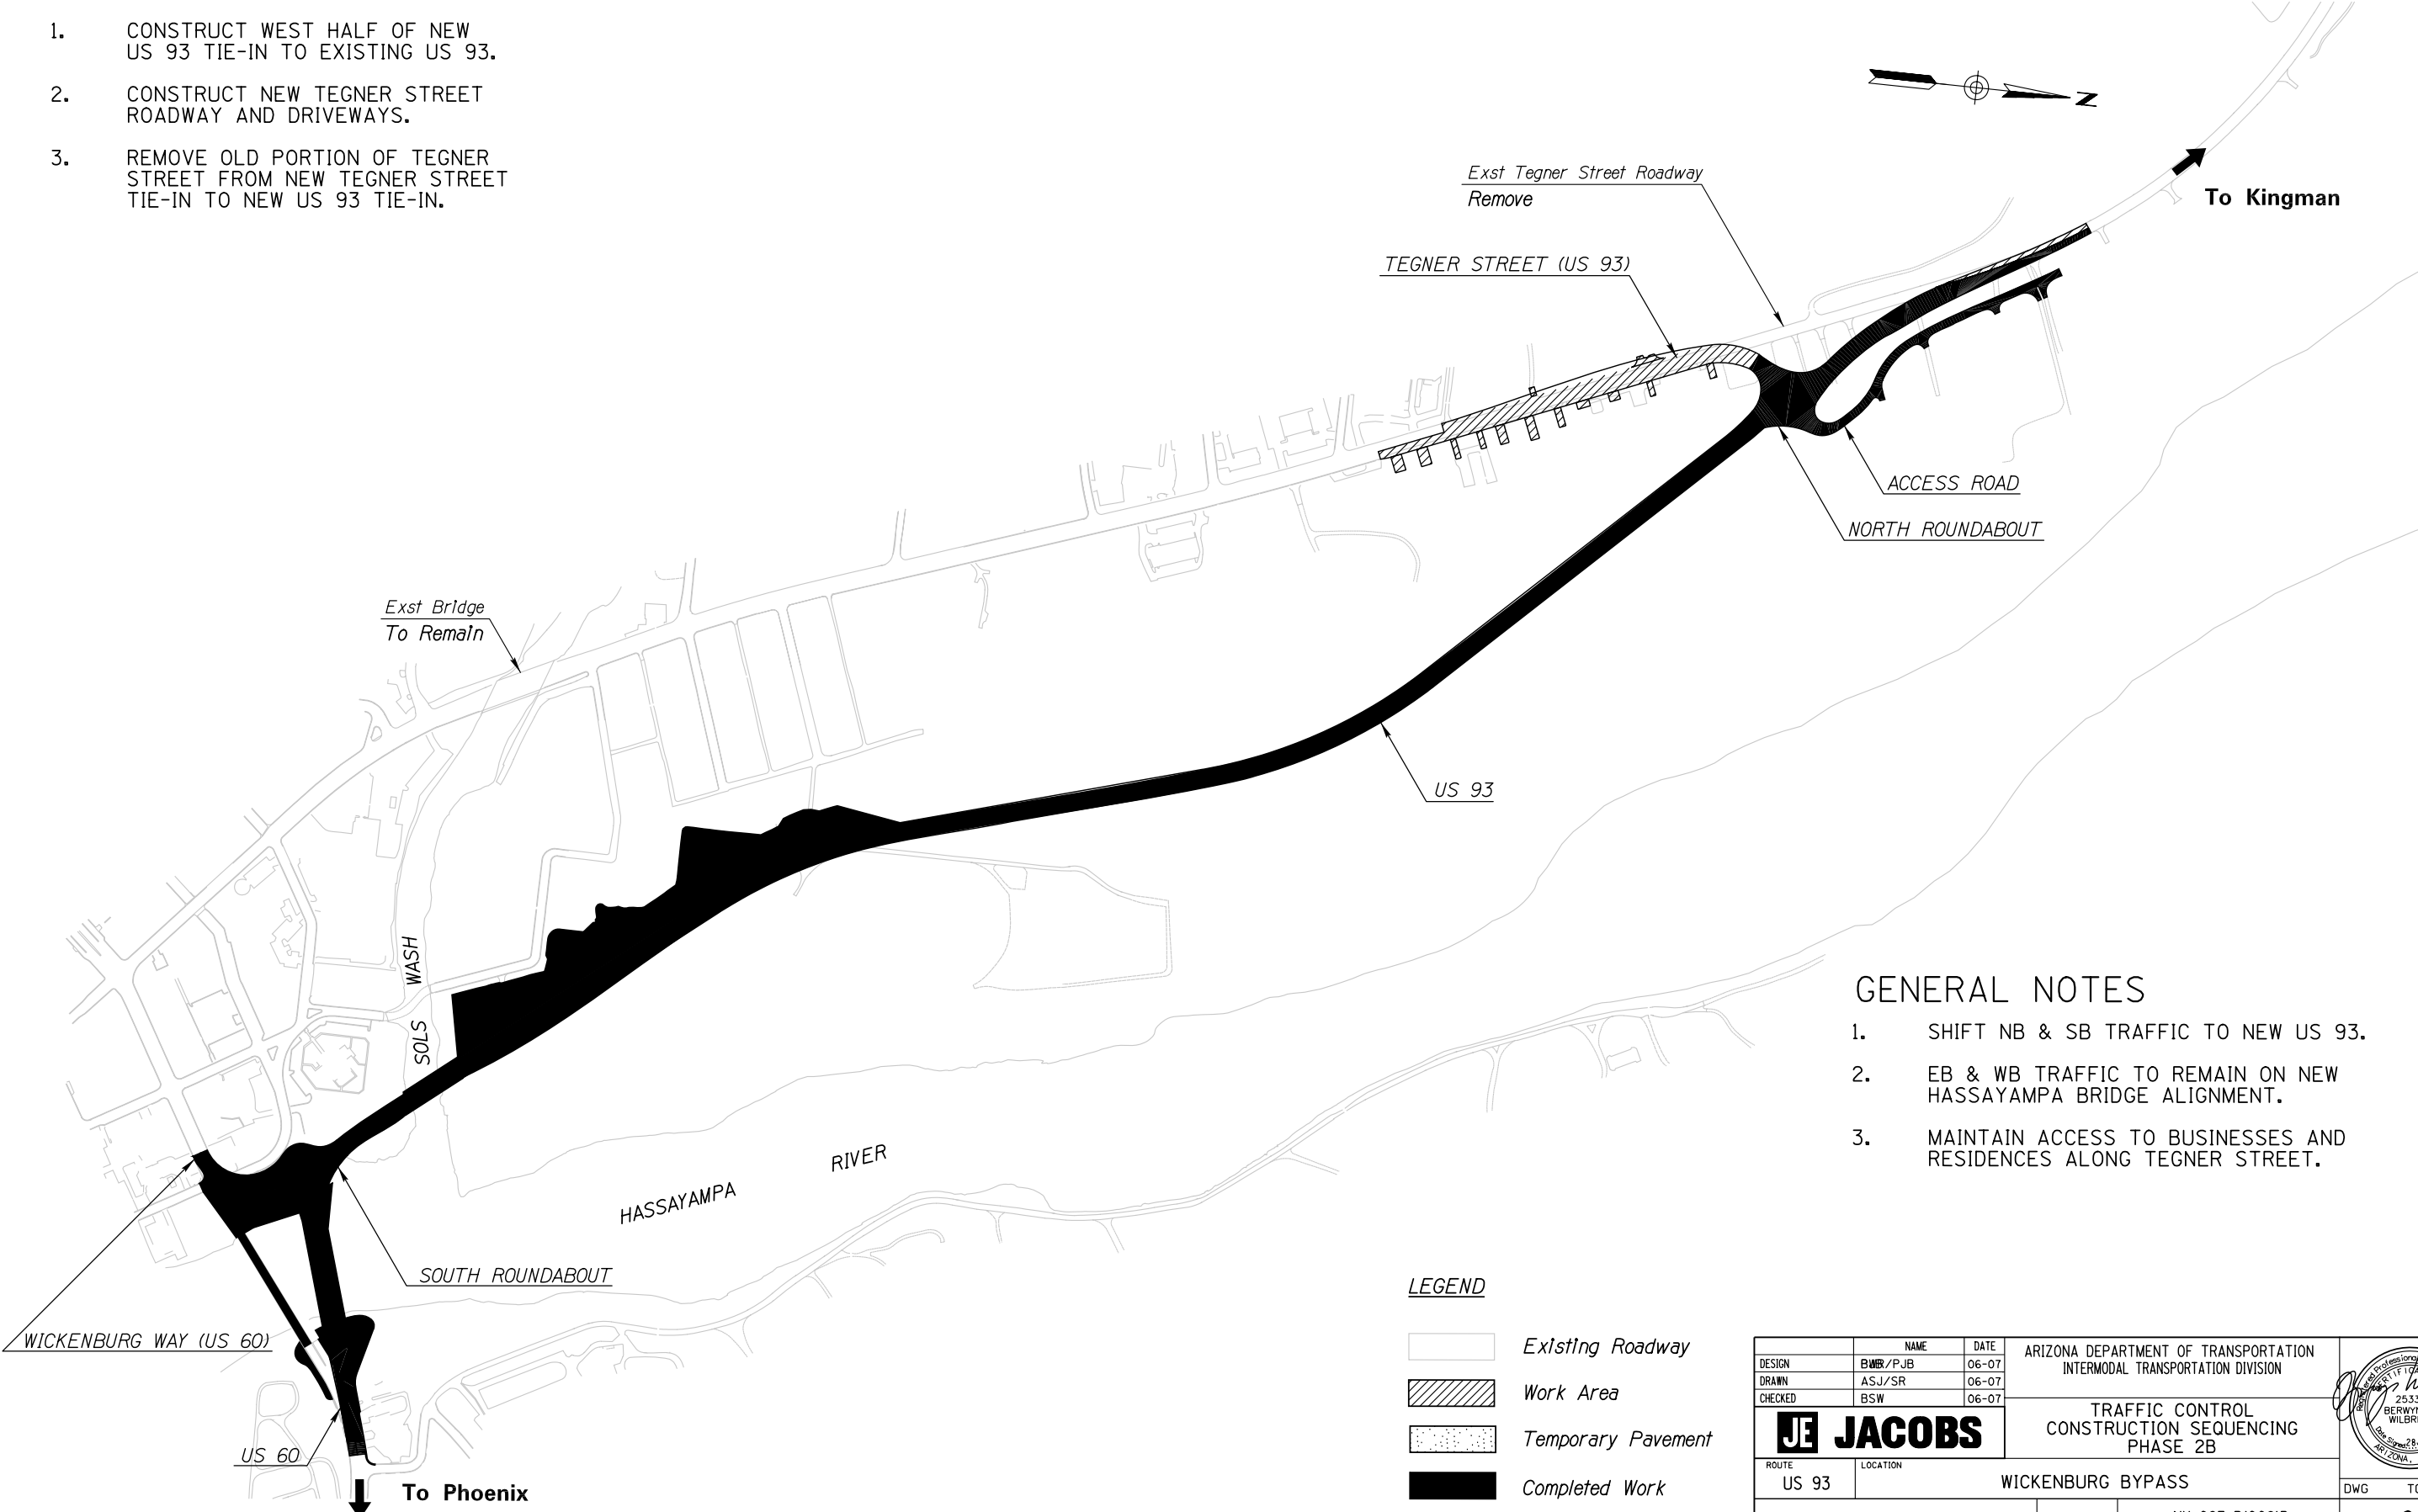

GENERAL NOTES

1. SHIFT NB & SB TRAFFIC TO NEW US 93.
2. EB & WB TRAFFIC TO REMAIN ON NEW HASSAYAMPA BRIDGE ALIGNMENT.
3. MAINTAIN ACCESS TO BUSINESSES AND RESIDENCES ALONG TEGNER STREET.

LEGEND

- Existing Roadway
- Work Area
- Temporary Pavement
- Completed Work


		NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION		
DESIGN	BMBR/PJB		06-07			
DRAWN	ASJ/SR		06-07			
CHECKED	BSW		06-07	TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 2B		
ROUTE		LOCATION				
US 93		WICKENBURG BYPASS		DWG TC07		
TRACS NO. H 5825 01C			NH-093-B(008)B			___ OF ___

DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	152	380	
93 MA 198					

PHASE 3A CONSTRUCTION

1. RESURFACE EAST HALF OF TEGNER STREET.

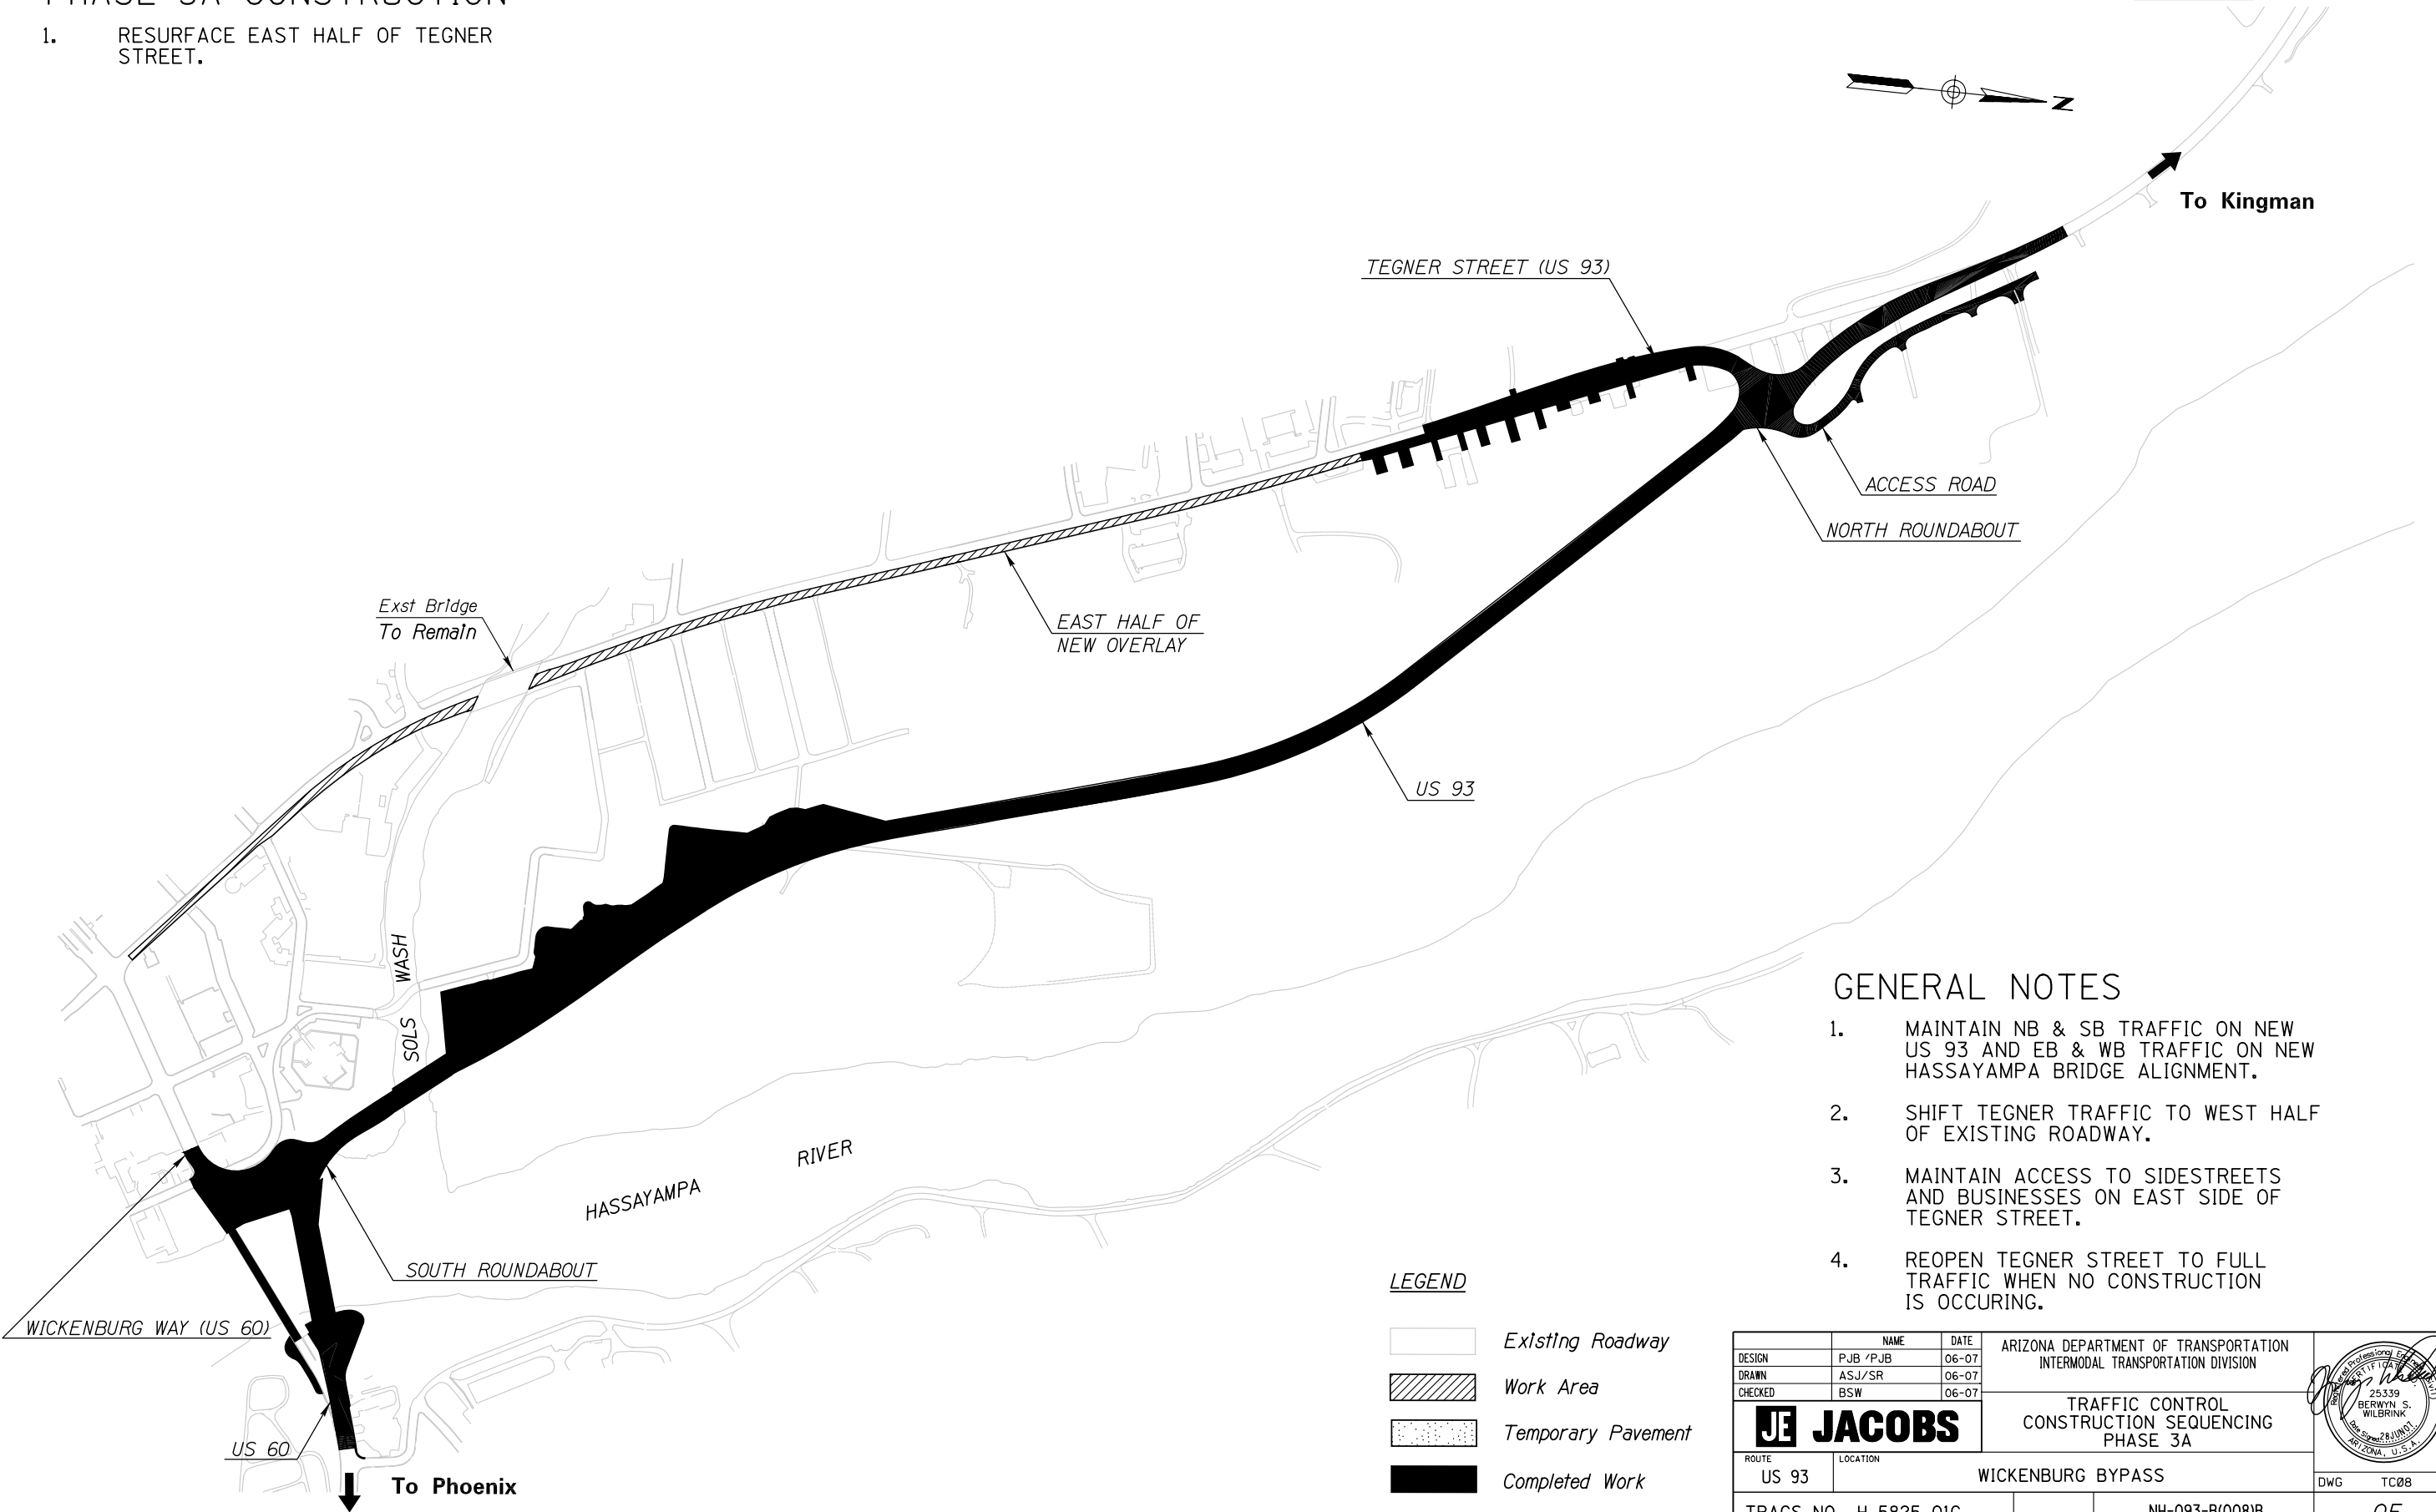



DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	153	380	
93 MA 198					

PHASE 3B CONSTRUCTION

1. RESURFACE WEST HALF OF TEGNER STREET.

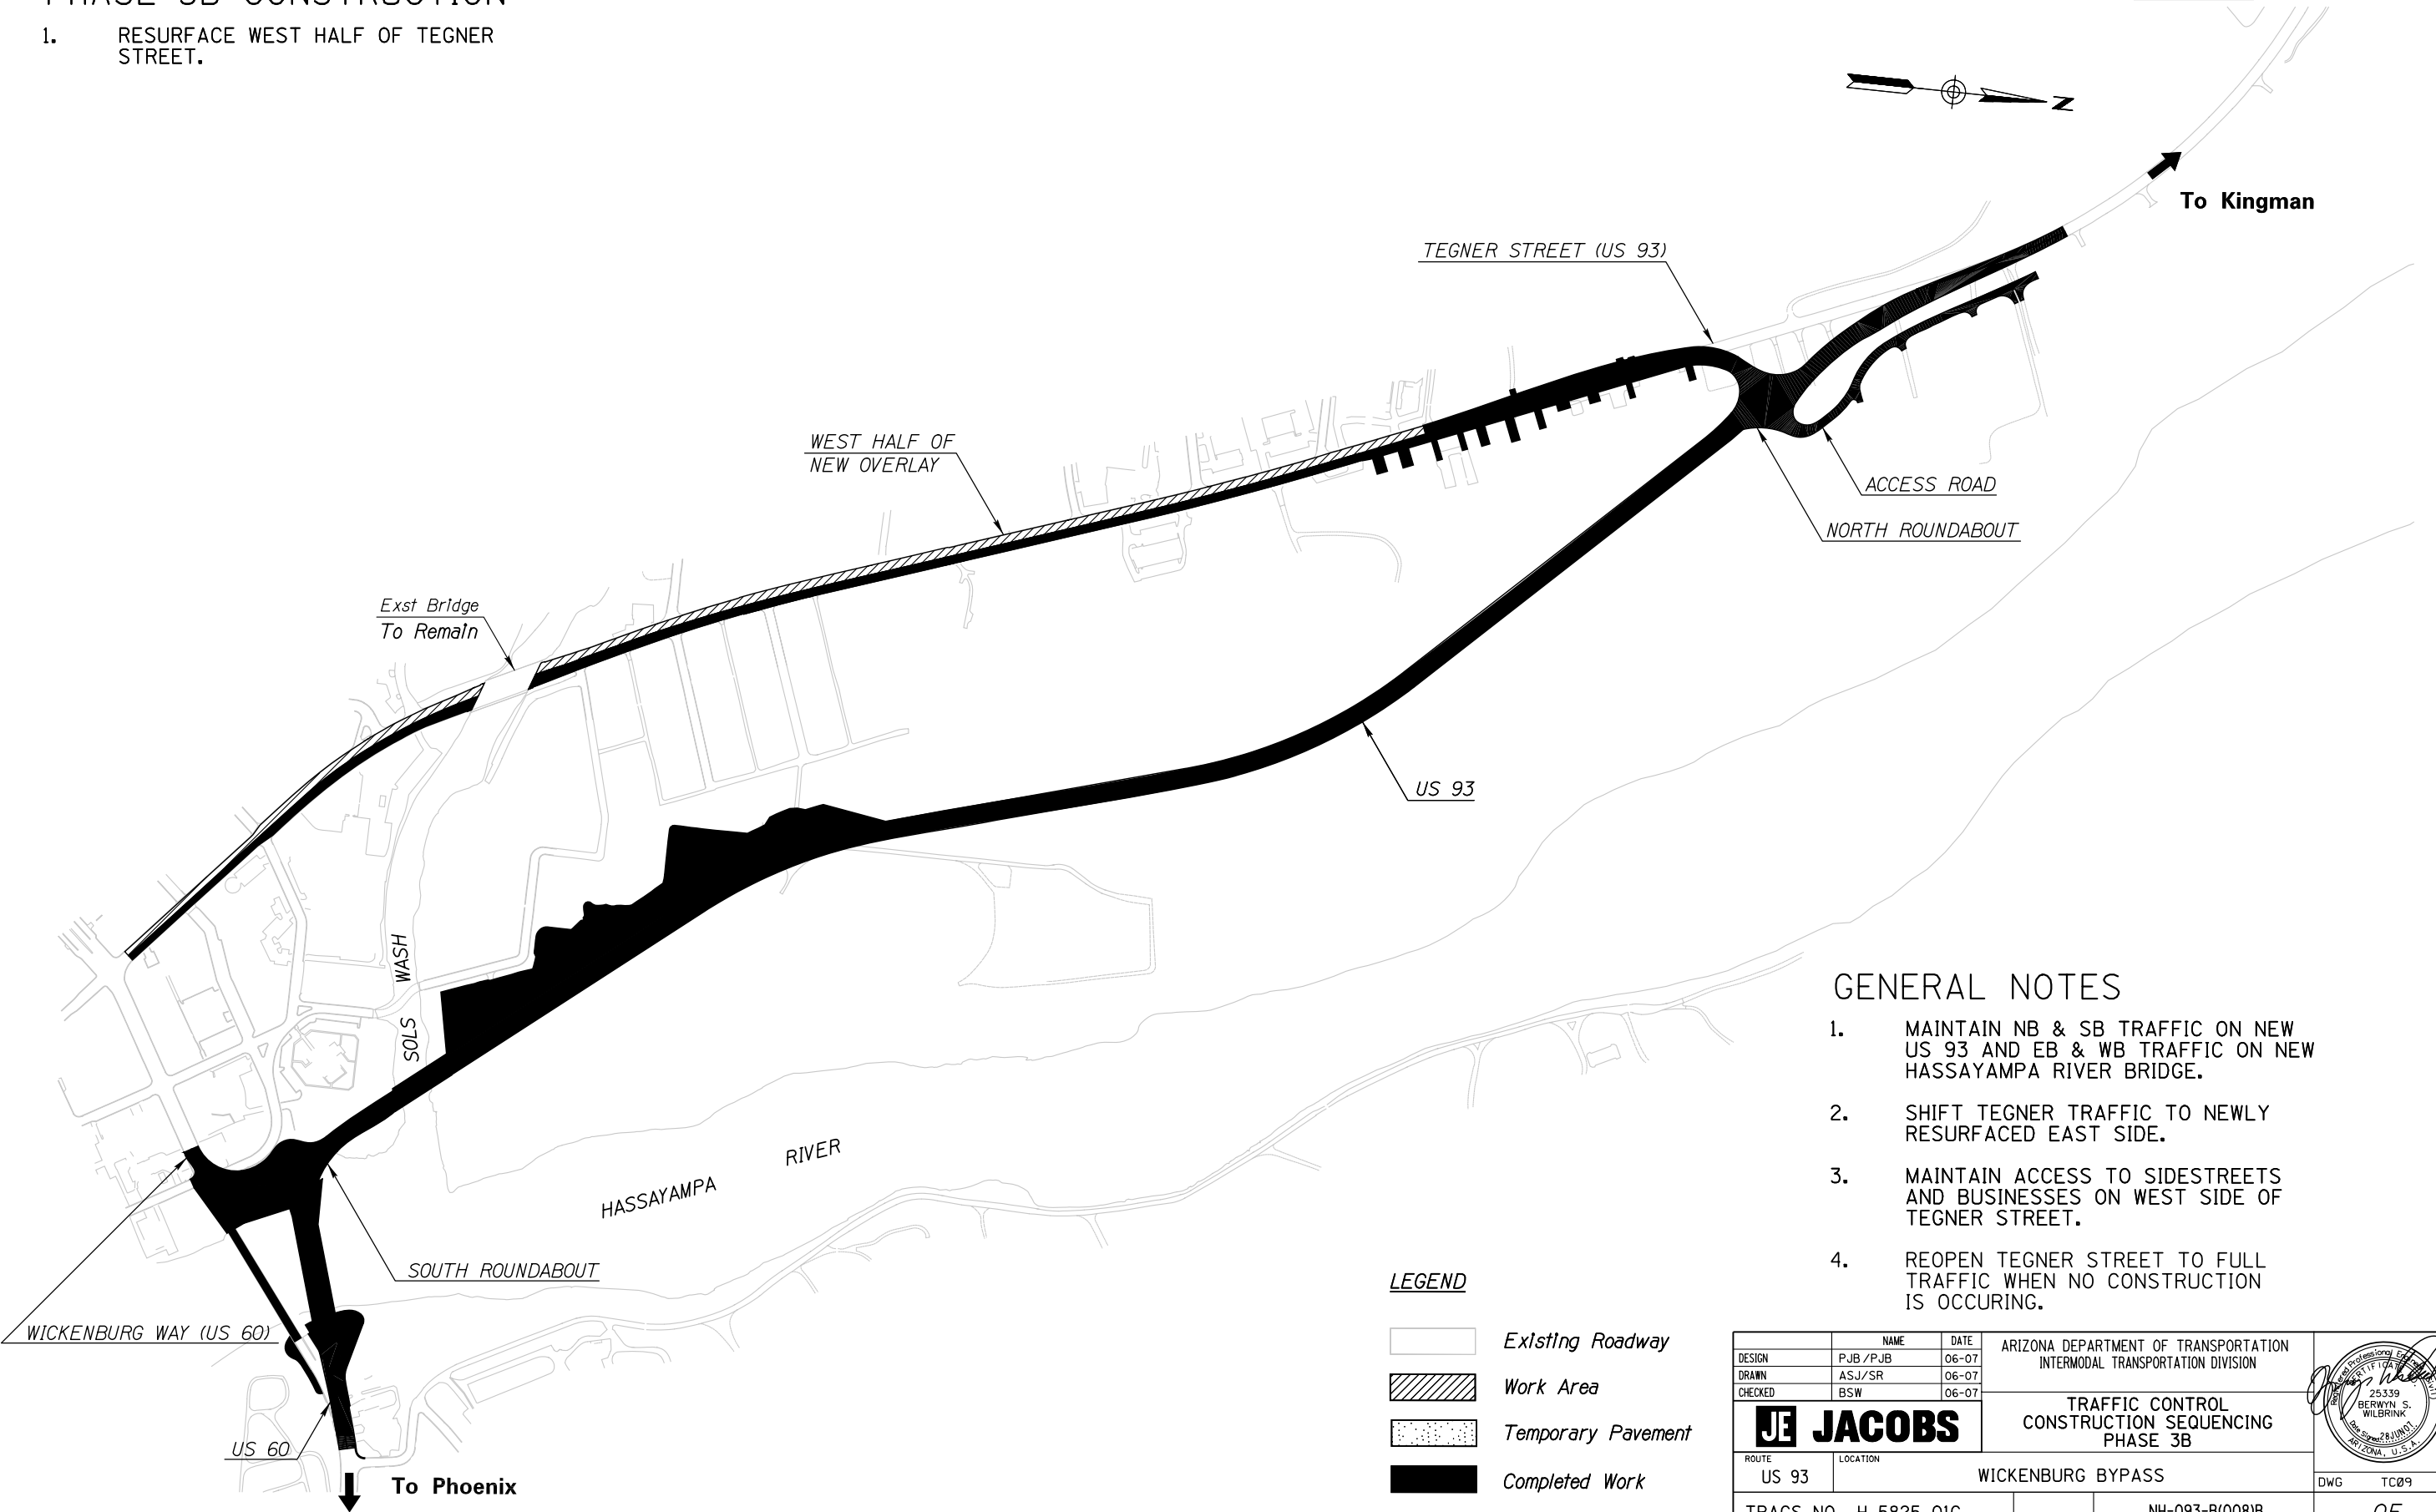

		NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION		
DESIGN	PJB / PJB		06-07			
DRAWN	ASJ / SR		06-07			
CHECKED	BSW		06-07			
 <b>JACOBS</b>				TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 3B		
ROUTE		LOCATION				
US 93		WICKENBURG BYPASS				DWG TC09
TRACS NO. H 5825 01C				NH-093-B(008)B		___ OF ___


DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO. DATE- LOCATION- REVISIONS- FINISHED PLANS- SURVEY NO.

F.H.W.A. REGION	STATE	PROJECT NO.	SHEET NO.	TOTAL SHEETS	AS BUILT
9	ARIZ.	NH-093-B(008)B	154	380	

93 MA 198

PHASE 4 CONSTRUCTION

1. STRIPE TEGNER STREET.
2. REMOVE TRAFFIC CONTROL ADVANCE WARNING SIGNS.



To Kingman

TEGNER STREET (US 93)

ACCESS ROAD

NORTH ROUNDABOUT

Exst Bridge  
To Remain

US 93

GENERAL NOTES

1. MAINTAIN NB & SB TRAFFIC ON NEW US 93 AND EB & WB TRAFFIC ON US 60.

SOUTH ROUNDABOUT

WICKENBURG WAY (US 60)

US 60

To Phoenix

LEGEND

- Existing Roadway
- Work Area
- Temporary Pavement
- Completed Work

		NAME	DATE	ARIZONA DEPARTMENT OF TRANSPORTATION INTERMODAL TRANSPORTATION DIVISION			
DESIGN	PJB /PJB		06-07				
DRAWN	ASJ/SR		06-07				
CHECKED	BSW		06-07	TRAFFIC CONTROL CONSTRUCTION SEQUENCING PHASE 4			
ROUTE		LOCATION		WICKENBURG BYPASS		DWG	TC10
US 93							
TRACS NO. H 5825 01C				NH-093-B(008)B		___ OF ___	
